



Progress Report

Executive Overview & Valuation Summary

06-Aug-26

CONTRACT AMOUNT
SAR 1,292,000.00
Authoritative baseline

EARNED VALUATION
SAR 353,364.60
27.35% Net Complete

REMAINING BALANCE
SAR 938,635.40
72.65% Balance

PROJECT TIMELINE
38 Days
Total: 154 Days

PROJECT INFORMATION

Status as of 06-Aug-26

Project Name:	GHEZLAN Project
Client:	AL ZAMIL
Contractor:	KAYAN CAPITAL HOLDINGS
PO Number:	HSP-PO-46319 (Revision 0)
Project Start Date:	30-Jun-26
Project End Date:	30-Nov-26
Contract Project Amount:	SAR 1,292,000.00
Net Physical Progress:	27.35%
Project Leader:	ERFAN AHMAD
Project Duration:	154 Calendar Days (Inclusive)
Timeline Day Number:	38 Days




Progress Report

Project Scope & Progress Valuation

06-Aug-26

Scope Analytics & Distribution

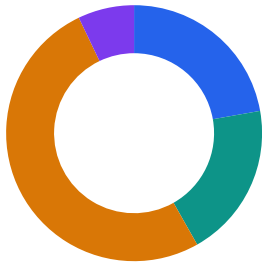

SCOPE WEIGHTAGE DISTRIBUTION

● FA GENERAL	22.2%	287,524.10 SAR
● FA FM 200	19.6%	253,518.84 SAR
● FIRE FIGHTING	51.1%	661,487.00 SAR
● FAT	7.1%	92,000.00 SAR


Project Scope Breakdown

Project: GHEZLAN Project (SAR) • 4 Activities

DESCRIPTION	TOTAL PRICE	WEIGHTAGE	PHYSICAL %	NET %	PROGRESS VALUE
FA GENERAL	287,524.10	22.25%	34.5%	7.68%	99,195.81
FA FM 200	253,518.84	19.62%	45.2%	8.87%	114,564.07
FIRE FIGHTING	661,487.00	51.20%	14.2%	7.24%	93,604.71
FAT	92,000.00	7.12%	50.0%	3.56%	46,000.00
Total Progress	1,292,000.00	100.20%	—	27.35%	353,364.60

OVERALL PHYSICAL COMPLETION

27.35%



TOTAL EARNED VALUATION

SAR 353,364.60

Authoritative Contract Value: SAR 1,292,000.00
